

Work Order ID 138649

November 06, 2015 10:15:00 AM

U/R

138649

Page 1

Item ID: D350-748-203

Accept

N900040100

Setup Start

NS1

Revision ID: URF 15-561

Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Stop

NS2

Start Date: 11/6/2015 Start Qty: 1.00

1

Cust Item ID:

Required Date: 11/20/2015 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan:

SA

Date: 0151106

Tooling:

Date:

Run Start

NR1

QC:

Date:

SPC (Y/N):

Date:

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr

Revision Nbr

D350-748-243

A U/R

OK

15/11/10

DAS

6

MW

15-11-26

100

Document Control

0.00

100

DOCUMENT CONTROL

DC

Memo

0.00

Doc.Control -USB or Paperwork

Photocopy bluefile & type labels per PPPD350-748-201

CHG001

DAS

27

9-89

JAN 19 2016

110

0.00

110

BENDING MACHINE - CROSSTUBES

CNC Bend 2

Memo

0.00

CNC Alpha 160 Bender

Bend tube as per Dwg D350-748-243 using CNC bender program D350A and Folio FT

*****UNDER BEND .225" PER SIDE*****

USE (4) DT9824 SHIM BLOC TO CHECK STRAIGHTNESS

TW

15-11-13

D350-748-203/138649

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : _____							
Misidentified	☐	Past Due	☐								

Work Order ID 138649***138649***

Page 2

November 06, 2015 10:15:00 AM

Item ID: D350-748-203 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: URF 15-561 Stop ***NS2***
Item Name: AS350 / AS355 Stainless Steel Aft Crosstube
Start Date: 11/6/2015 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 11/20/2015 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

120

0.00

120

Crosstubes

Memo

0.00

Crosstubes

VERIFY CROSSTUBE DIMENSIONS AS PER DWG

12/1
15-11-20DAS
9
9-89

127

QC15- Crosstube Dimensional Check

0.00

127

QC

Memo

0.00

Quality Control

MARK CUT LINES

DAS
03
9-89

DP 15-11-16

128

0.00

128

Crosstubes

Memo

0.00

Crosstubes

CUT TUBE AT HEIGHT ON FAI SHEET

VERF HEIGHT 31.35 BY QC 15 LEVEL INSPECTOR EBVERF TWIST 0 BY QC15 LEVEL INSPECTOR EB

BL 15/11/16

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width:100%; border: none;"> <tr> <td style="width:15%;">Skid-tube ☐</td> <td style="width:15%;">Cross tube ☐</td> <td style="width:15%;">Water Jet ☐</td> <td style="width:15%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐																																															
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																																																																				
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																																																																				
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																																																																				
Large Fab ☐	Composite ☐	Supplier ☐																																																																					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____																																																																
Description Work Order Deviation				Disposition																																																																			
Root Cause <table style="width:100%; border: none;"> <tr><td>Environment ☐</td><td>No Re-verification ☐</td></tr> <tr><td>Design ☐</td><td>Operator ☐</td></tr> <tr><td>Doc/Data ☐</td><td>Offset/Setup ☐</td></tr> <tr><td>Equip/Tooling ☐</td><td>Supplier ☐</td></tr> <tr><td>Handling/Pre ☐</td><td>Training ☐</td></tr> <tr><td>Material ☐</td><td>Use for Testing ☐</td></tr> <tr><td>Internal Transport ☐</td><td>Poor Information ☐</td></tr> <tr><td>Tribal Knowledge ☐</td><td>Rushing ☐</td></tr> <tr><td>LOA ☐</td><td>Product Improvement ☐</td></tr> <tr><td>Substation ☐</td><td>Process Improvement ☐</td></tr> <tr><td>Past Expiry Date ☐</td><td>Manufacturing Process ☐</td></tr> <tr><td>Misidentified ☐</td><td>Past Due ☐</td></tr> </table>		Environment ☐	No Re-verification ☐	Design ☐	Operator ☐	Doc/Data ☐	Offset/Setup ☐	Equip/Tooling ☐	Supplier ☐	Handling/Pre ☐	Training ☐	Material ☐	Use for Testing ☐	Internal Transport ☐	Poor Information ☐	Tribal Knowledge ☐	Rushing ☐	LOA ☐	Product Improvement ☐	Substation ☐	Process Improvement ☐	Past Expiry Date ☐	Manufacturing Process ☐	Misidentified ☐	Past Due ☐	FAULT CATEGORY <table style="width:100%; border: none;"> <tr> <td style="width:25%;">Pressure/Forced ☐</td> <td style="width:25%;">Temperature/Cure ☐</td> <td style="width:25%;">Power Loss/Surge ☐</td> <td style="width:25%;">Positioned Wrong ☐</td> </tr> <tr> <td>Bending ☐</td> <td>Set-up ☐</td> <td>Folio/Program ☐</td> <td>Outside Dimensions ☐</td> </tr> <tr> <td>Centre Not Concentric ☐</td> <td>BOM/Route ☐</td> <td>Grain ☐</td> <td>Over/Under tolerance ☐</td> </tr> <tr> <td>Cracks ☐</td> <td>Broken/Damage/Defect ☐</td> <td>Weld ☐</td> <td>Part Incorrect ☐</td> </tr> <tr> <td>Crimp/Kink/Ripple/Wave ☐</td> <td>Inspection Incomplete/Unqualified ☐</td> <td>Wrong Stock Pulled ☐</td> <td>Part Lost/Missing ☐</td> </tr> <tr> <td>Cuffs ☐</td> <td>Contamination ☐</td> <td>Out of Sequence ☐</td> <td>Part Moved ☐</td> </tr> <tr> <td>Crushing ☐</td> <td>Countersink ☐</td> <td>Off-set ☐</td> <td>Drawing ☐</td> </tr> <tr> <td>Heat Treat ☐</td> <td>Cut Too Short ☐</td> <td>Mislabeled ☐</td> <td>Finish ☐</td> </tr> <tr> <td>Wave/Twist in Tube ☐</td> <td>Instructions Incomplete/Unclear ☐</td> <td>Fit/Function ☐</td> <td>Misread ☐</td> </tr> <tr> <td>Marks/Chatter ☐</td> <td>Drill Holes ☐</td> <td>Misaligned/off center ☐</td> <td>Turning Sequence ☐</td> </tr> </table>						Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐
Environment ☐	No Re-verification ☐																																																																						
Design ☐	Operator ☐																																																																						
Doc/Data ☐	Offset/Setup ☐																																																																						
Equip/Tooling ☐	Supplier ☐																																																																						
Handling/Pre ☐	Training ☐																																																																						
Material ☐	Use for Testing ☐																																																																						
Internal Transport ☐	Poor Information ☐																																																																						
Tribal Knowledge ☐	Rushing ☐																																																																						
LOA ☐	Product Improvement ☐																																																																						
Substation ☐	Process Improvement ☐																																																																						
Past Expiry Date ☐	Manufacturing Process ☐																																																																						
Misidentified ☐	Past Due ☐																																																																						
Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																																																																				
Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																																																																				
Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																																																																				
Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐																																																																				
Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																																																																				
Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																																																																				
Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐																																																																				
Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐																																																																				
Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																																																																				
Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																																																																				
		OTHER : _____																																																																					

Work Order ID 138649

November 06, 2015 10:15:00 AM

138649

Page 3

Item ID: D350-748-203

Accept

N900040100

Setup Start

NS1

Revision ID: URF 15-561

Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Stop

NS2

Start Date: 11/6/2015 Start Qty: 1.00

1

Cust Item ID:

Required Date: 11/20/2015 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

130

0.00

130

Crosstubes

Crosstubes

Memo

0.00

2- Drill Tube as per Dwg D350-748-243 Using DT8876 Drill Jigs,
Set-up drill table as per QSI 010

3 -Deburr

4- Engrave Part # and Batch # as per Dwg D350-748-243

5-Remove all marks from tube within limits of D350-748-243

BC

15/11/18

BC

15/11/19

140

140

QC

Quality Control

QC- Inspect dimensions to drawing

0.00

Memo

0.00

QC DAS
9-89 15-11-20

15-11-20

DAS
9
9-89

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause			FAULT CATEGORY				
Environment	☐	No Re-verification	☐	Pressure/Forced	Temperature/Cure	☐	Power Loss/Surge
Design	☐	Operator	☐	Bending	Set-up	☐	Folio/Program
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	BOM/Route	☐	Grain
Equip/Tooling	☐	Supplier	☐	Cracks	Broken/Damage/Defect	☐	Weld
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled
Material	☐	Use for Testing	☐	Cuffs	Contamination	☐	Out of Sequence
Internal Transport	☐	Poor Information	☐	Crushing	Countersink	☐	Off-set
Tribal Knowledge	☐	Rushing	☐	Heat Treat	Cut Too Short	☐	Mislabeled
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	Instructions Incomplete/Unclear	☐	Fit/Function
Substation	☐	Process Improvement	☐	Marks/Chatter	Drill Holes	☐	Misaligned/off center
Past Expiry Date	☐	Manufacturing Process	OTHER :				
Misidentified	☐	Past Due					

Work Order ID 138649***138649***

Page 4

November 06, 2015 10:15:00 AM

Item ID: D350-748-203

Accept

N900040100

Setup Start

NS1

Revision ID: URF 15-561

Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Stop

NS2

Start Date: 11/6/2015 Start Qty: 1.00

1

Cust Item ID:

Required Date: 11/20/2015 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start

NR1

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
174	Outsource process - NDT per QSI038 4.1	0.00							
174									
Outsource2	Memo	0.00							
Outsource process - NDT	ISSUE P/O TO ACCUREN: <u>30533</u>								
176	Receive & Inspect for Damage & Mat'l Certs	0.00							
176									
Packaging	Memo	0.00							
Packaging									
178	QC5- Inspect part completeness to step on W/O	0.00							
178									
QC	Memo	0.00							
Quality Control									

CL NOV 23 2015 1IX SP15-11-23DAS
38
9-89

DEC 03 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

Work Order ID 138649

138649

Page 5

November 06, 2015 10:15:00 AM

Item ID: D350-748-203

Accept

N900040100

Setup Start

NS1

Revision ID: URF 15-561

Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Stop

NS2

Start Date: 11/6/2015 Start Qty: 1.00

1

Cust Item ID:

Required Date: 11/20/2015 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan:

Date:

Tooling:

Date:

Run Start

NR1

QC:

Date:

SPC (Y/N):

Date:

Stop

NR2

Sequence ID/
Work Center ID

Operation
Description

Set Up/
Run Hours

Tool ID

Tool #

Plan
Code

Accept
Qty

Reject
Qty

Reject
Number

Insp.
Stamp

180

0.00

180

SprayPaint

SprayPaint

Spray Painting

Memo

0.00

1-Prime inside and out crosstube as per QSI 005 4.2

BATCH: 133084

2-Paint Outside of Tube as per Dart QSI 005 4.2

BATCH: 133325

DAS

41

9-89

15-11-25

190

QC14- Inspect Spray Paint

0.00

190

QC

Quality Control

Memo

0.00

Then, Wrap in plastic bag to protect from scratches

DAS

38

9-89

DEC 03 2015

DQA:

Date: 16/02/04



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: ~~16/02/03~~

Date: 16/02/03

Work Order update only ☐

Work Order: <u>138649</u> Part No. <u>D380-748-203</u> NCR No. <u>16-5566</u>	DISPOSITION Rework ☒ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS <table style="width:100%;"> <tr> <td>Skid-tube ☐</td> <td>Cross tube ☒</td> <td>Water Jet ☐</td> <td>Engineering ☒</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>			Skid-tube ☐	Cross tube ☒	Water Jet ☐	Engineering ☒	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐																																																
Skid-tube ☐	Cross tube ☒	Water Jet ☐	Engineering ☒																																																																
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																																																																
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																																																																
Large Fab ☐	Composite ☐	Supplier ☐																																																																	
Date: <u>15/11/6</u>	Step #: <u>180</u>	QTY Effective: <u>2</u>	MRB (QSI042) Approval DAS 12 9-89 <u>15/11/6</u>																																																																
Description Work Order Deviation		Disposition																																																																	
USE AXALTA PRE-TREATMENT PER QSI UDS		AXALTA 1320SS Cleaner B/N 132520 AXALTA 230S Adhesion Promoter B/N 132474																																																																	
		Completed By DAS 41 9-89 <u>15-11-25</u> Lead hand / Supervisor Approval Verification DAS 9 9-89 <u>16-01-19</u> QC / QA Coordinator DAS Approval 9 9-89 <u>16-01-19</u>																																																																	
Root Cause <table style="width:100%;"> <tr> <td>Environment ☐</td> <td>No Re-verification ☐</td> </tr> <tr> <td>Design ☐</td> <td>Operator ☐</td> </tr> <tr> <td>Doc/Data ☐</td> <td>Offset/Setup ☐</td> </tr> <tr> <td>Equip/Tooling ☐</td> <td>Supplier ☐</td> </tr> <tr> <td>Handling/Pre ☐</td> <td>Training ☐</td> </tr> <tr> <td>Material ☐</td> <td>Use for Testing ☐</td> </tr> <tr> <td>Internal Transport ☐</td> <td>Poor Information ☐</td> </tr> <tr> <td>Tribal Knowledge ☐</td> <td>Rushing ☐</td> </tr> <tr> <td>LOA ☐</td> <td>☒ Product Improvement</td> </tr> <tr> <td>Substation ☐</td> <td>Process Improvement ☐</td> </tr> <tr> <td>Past Expiry Date ☐</td> <td>Manufacturing Process ☐</td> </tr> <tr> <td>Misidentified ☐</td> <td>Past Due ☐</td> </tr> </table>		Environment ☐	No Re-verification ☐	Design ☐	Operator ☐	Doc/Data ☐	Offset/Setup ☐	Equip/Tooling ☐	Supplier ☐	Handling/Pre ☐	Training ☐	Material ☐	Use for Testing ☐	Internal Transport ☐	Poor Information ☐	Tribal Knowledge ☐	Rushing ☐	LOA ☐	☒ Product Improvement	Substation ☐	Process Improvement ☐	Past Expiry Date ☐	Manufacturing Process ☐	Misidentified ☐	Past Due ☐	FAULT CATEGORY <table style="width:100%;"> <tr> <td>Pressure/Forced ☐</td> <td>Temperature/Cure ☐</td> <td>Power Loss/Surge ☐</td> <td>Positioned Wrong ☐</td> </tr> <tr> <td>Bending ☐</td> <td>Set-up ☐</td> <td>Folio/Program ☐</td> <td>Outside Dimensions ☐</td> </tr> <tr> <td>Centre Not Concentric ☐</td> <td>BOM/Route ☐</td> <td>Grain ☐</td> <td>Over/Under tolerance ☐</td> </tr> <tr> <td>Cracks ☐</td> <td>Broken/Damage/Defect ☐</td> <td>Weld ☐</td> <td>Part Incorrect ☐</td> </tr> <tr> <td>Crimp/Kink/Ripple/Wave ☐</td> <td>Inspection Incomplete/Unqualified ☐</td> <td>Wrong Stock Pulled ☐</td> <td>Part Lost/Missing ☐</td> </tr> <tr> <td>Cuffs ☐</td> <td>Contamination ☐</td> <td>Out of Sequence ☐</td> <td>Part Moved ☐</td> </tr> <tr> <td>Crushing ☐</td> <td>Countersink ☐</td> <td>Off-set ☐</td> <td>☒ Drawing</td> </tr> <tr> <td>Heat Treat ☐</td> <td>Cut Too Short ☐</td> <td>Mislabeled ☐</td> <td>☒ Finish</td> </tr> <tr> <td>Wave/Twist in Tube ☐</td> <td>Instructions Incomplete/Unclear ☐</td> <td>Fit/Function ☐</td> <td>Misread ☐</td> </tr> <tr> <td>Marks/Chatter ☐</td> <td>Drill Holes ☐</td> <td>Misaligned/off center ☐</td> <td>Turning Sequence ☐</td> </tr> </table>		Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Crushing ☐	Countersink ☐	Off-set ☐	☒ Drawing	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	☒ Finish	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐
Environment ☐	No Re-verification ☐																																																																		
Design ☐	Operator ☐																																																																		
Doc/Data ☐	Offset/Setup ☐																																																																		
Equip/Tooling ☐	Supplier ☐																																																																		
Handling/Pre ☐	Training ☐																																																																		
Material ☐	Use for Testing ☐																																																																		
Internal Transport ☐	Poor Information ☐																																																																		
Tribal Knowledge ☐	Rushing ☐																																																																		
LOA ☐	☒ Product Improvement																																																																		
Substation ☐	Process Improvement ☐																																																																		
Past Expiry Date ☐	Manufacturing Process ☐																																																																		
Misidentified ☐	Past Due ☐																																																																		
Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐																																																																
Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐																																																																
Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐																																																																
Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐																																																																
Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐																																																																
Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐																																																																
Crushing ☐	Countersink ☐	Off-set ☐	☒ Drawing																																																																
Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	☒ Finish																																																																
Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐																																																																
Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐																																																																
OTHER: ☐																																																																			

Work Order ID 138649

138649

Page 6

November 06, 2015 10:15:00 AM

Item ID: D350-748-203 Accept *N900040100* Setup Start *NS1*
 Revision ID: URF 15-561 Stop *NS2*
 Item Name: AS350 / AS355 Stainless Steel Aft Crosstube
 Start Date: 11/6/2015 Start Qty: 1.00 *1* Cust Item ID:
 Required Date: 11/20/2015 Req'd Qty: 1.00 *1* Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
200	Crosstubes	0.00				1			DAS 41 9-89 15-11-26
200									
Crosstubes	Memo	0.00							
Crosstubes	INSTALL GROUND WIRE INSERT, THEN INSERT SCREW AND WASHER								
	1-Abrade mating surfaces of support and crosstube with 180 grit sandpaper, clean the area with MEK or equivalent as per dwg								
	2-Install supports with Proseal 890 per D350-748-243 and QSI 015								
	A/R Proseal 890 Batch: 133071								
	EXP: 2/16								
	3-Install supports clamps Using Dt8876 as per Dwg D350-748-243, Torque to 60-80 IN-LBS.								
	PROSEAL CURE TIME 72 HOURS:								
	Start: 15-11-26								
	Finish: 15-11-29								
210	QC5- Inspect part completeness to step on W/O	0.00				1			DAS 38 8-89 DEC 03 2015
210									
QC	Memo	0.00							
Quality Control	***RE-CHECK TORCQUE ON CLAMP AFTER PROSEAL HAS CURED FOR 72HOURS AS PER DWG.***								

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY																																																																																																																											
Environment	☐	Design	☐	Doc/Data	☐	Equip/Tooling	☐	Handling/Pre	☐	Material	☐	Internal Transport	☐	Tribal Knowledge	☐	LOA	☐	Substation	☐	Past Expiry Date	☐	Misidentified	☐	No Re-verification	☐	Operator	☐	Offset/Setup	☐	Supplier	☐	Training	☐	Use for Testing	☐	Poor Information	☐	Rushing	☐	Product Improvement	☐	Process Improvement	☐	Manufacturing Process	☐	Past Due	☐	Pressure/Forced	☐	Bending	☐	Centre Not Concentric	☐	Cracks	☐	Crimp/Kink/Ripple/Wave	☐	Cuffs	☐	Crushing	☐	Heat Treat	☐	Wave/Twist in Tube	☐	Marks/Chatter	☐	Temperature/Cure	☐	Set-up	☐	BOM/Route	☐	Broken/Damage/Defect	☐	Inspection Incomplete/Unqualified	☐	Contamination	☐	Countersink	☐	Cut Too Short	☐	Instructions Incomplete/Unclear	☐	Drill Holes	☐	Power Loss/Surge	☐	Folio/Program	☐	Grain	☐	Weld	☐	Wrong Stock Pulled	☐	Out of Sequence	☐	Off-set	☐	Mislabeled	☐	Fit/Function	☐	Misaligned/off center	☐	Positioned Wrong	☐	Outside Dimensions	☐	Over/Under tolerance	☐	Part Incorrect	☐	Part Lost/Missing	☐	Part Moved	☐	Drawing	☐	Finish	☐	Misread	☐	Turning Sequence	☐
																								OTHER : ☐																																																																																																							

November 06, 2015 10:15:00 AM

Item ID: D350-748-203

Accept

N900040100

Setup Start *NS1*

Revision ID: URF 15-561

Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Stop *NS2*

Start Date: 11/6/2015 **Start Qty:** 1.00 ***1***

Cust Item ID:

Required Date: 11/20/2015 **Req'd Qty:** 1.00 ***1***

Customer:

Reference:

Approvals: **Process Plan:** _____ **Date:** _____ **Tooling:** _____ **Date:** _____

Run Start *NR1*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/
Work Center ID

Operation Description

Set Up/ Run Hours

Tool ID**Tool #**

Plan Code

Accept	Qty
--------	-----

Reject
Qty

Reject Number

**Insp.
Stamp**

250

QC21- Final Inspection - Work Order Release

0.00

250

QC

Memo

0.00

Quality Control

MLJ JAN 19 2016

MC5 JAN 19 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐				FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : ☐											

Picklist Print

November 06, 2015 10:15:05 AM

Page 1

Work Order ID: 138649

138649

Parent Item: D350-748-203

D350-748-203

Parent Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Start Date: 11/6/2015

Required Date: 11/20/2015

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP REV:A 15.03.23 NEW ISSUE DD VERF;JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D350-748-243TRN

Manufactured

No

Each

8.0000

1

D350-748-243TRN

Crosstube Installation, High Aft

1 BC 15/11/12

Location

Loc Qty

Loc Code

LG003

8

135163

1

135164

1

135165

1

135166

1

135167

1

135168

1

135169

1

135170

1

D3502-1

Manufactured

No

Each

28.0000

2

D3502-1

Support

DAS
41
9-89

15-11-27

Location

Loc Qty

Loc Code

LG052

28

130349

28

Each

74.0000

2

D5123-7

Manufactured

No

D5123-7

Clamp Cushion

DAS
41
9-89

15-11-27

Location

Loc Qty

Loc Code

LG052

74

131194

16

133492

12

136671

26

137766

20

2

Picklist Print

November 06, 2015 10:15:05 AM

Page 2

Work Order ID: 138649

138649

Parent Item: D350-748-203

D350-748-203

Parent Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Start Date: 11/6/2015

Required Date: 11/20/2015

Start Qty: 1.00

Required Qty: 1.00

AETC-1032

Purchased

No

Each

20.0000

1

DAS

AETC-1032

41

Insert

9-89

15-12-2

Location

Loc Qty

Loc Code

ST547

20

m133002

20

Each

1,068.000

1

DAS

NAS1149C0363R

Purchased

No

NAS1149C0363R

41

Washer

9-89

15-12-2

Location

Loc Qty

Loc Code

FP001

31

114742

31

GA

506

m133077

506

ST260a

494

m133077

494

ST271

37

m132763

37

MS21920-20

Purchased

No

MS21920-20

DAS

Clamp

41

9-89

15-11-27

Location

Loc Qty

Loc Code

FG

2

122254

2

LG050

25

m133483

25

LG056

130

m128650

13

m132675

67

m133134

50

November 06, 2015 10:15:05 AM

Shop Packet Print

Page 2

Picklist Print

November 06, 2015 10:15:05 AM

Page 3

Work Order ID: 138649

138649

Parent Item: D350-748-203

D350-748-203

Parent Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Start Date: 11/6/2015

Required Date: 11/20/2015

Start Qty: 1.00

Required Qty: 1.00

MS51958-63

Purchased

No

Each

41.0000

1

DAS
41

9-89

15-12-2

MS51958-63

Screw

Location

Loc Qty

Loc Code

ST273

41

m131886

41

NAS1149D0563J

Purchased

No

220

Each

1,227.000

8

8

NAS1149D0563.J

Washer

Location

Loc Qty

Loc Code

GA

53

m125807

53

ST260a

928

m130799

63

m132035

55

m132256

10

m133134

300

m133363

500

ST269

227

m128257

156

m132677

71

ST271

19

m131026

19

DAS
27
9-89

NOV 26 2015

DAS
6
9-89
DAS
28
9-89

?

Picklist Print

November 06, 2015 10:15:05 AM

Page 4

Work Order ID: 138649

138649

Parent Item: D350-748-203

D350-748-203

Parent Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Start Date: 11/6/2015

Required Date: 11/20/2015

Start Qty: 1.00

Required Qty: 1.00

MS21042L4

Purchased

No

220

Each

2,350.000

24

24

MS21042L4

Locknut

Location

Loc Qty

Loc Code

FP001

2

m124231

2

GA

67

m127813

67

ST260a

138

m130799

56

m131803

6

m132262

76

ST303

1974

m133363

1974

ST305

169

m128300

8

m130388

7

m130922

97

m132123

56

m133316

1

DAS
27
9-89

NOV 26 2015

DAS
28
9-89

24

Picklist Print

November 06, 2015 10:15:05 AM

Page 5

Work Order ID: 138649

138649

Parent Item: D350-748-203

D350-748-203

Parent Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Start Date: 11/6/2015

Required Date: 11/20/2015

Start Qty: 1.00

Required Qty: 1.00

MS21042L5

Purchased

No

220

Each

473.0000

4

4

MS21042L5

Nut

DAS
6
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

GA

146

m127813

146

ST303

79

m132677

79

ST304

200

m133363

200

ST305

48

m127813

19

m131340

21

m132123

8

DAS
27
9-89

AN4-41A

Purchased

No

220

Each

287.0000

8

8

AN4-41A

Bolt

DAS
28
9-89

Location

Loc Qty

Loc Code

ST312A

238

m130726

8

m132189

130

m133483

100

ST342

49

m130716

49

DAS
27
9-89

NOV 26 2015

DAS
6
9-89

Picklist Print

November 06, 2015 10:15:05 AM

Page 6

Work Order ID: 138649

138649

Parent Item: D350-748-203

D350-748-203

Parent Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Start Date: 11/6/2015

Required Date: 11/20/2015

Start Qty: 1.00

Required Qty: 1.00

D3501-1 Manufactured No

220 Each 419.0000 16 16

D3501-1

Bushing

BAS
27
9-89

Location	Loc Qty	Loc Code
ST039	112	
130742	14	
135919	98	
ST046	1	
125925	1	
ST051A	306	
135918	306	

DAS
8
9-89

DAS
28
9-89

NAS1149D0463J

Purchased No

220 Each 5,204.000 32 32

NAS1149D0463.J

WASHER

BAS
27
9-89

Location	Loc Qty	Loc Code
GA	626	
M129390	41	
M132035	585	
ST260a	3136	
M133284	1636	
M133316	1500	
ST269	1442	
M129682	47	
M130799	371	
M132317	101	
M132677	888	
M133077	35	

DAS
8
9-89

DAS
28
9-89

NOV 26 2015

Picklist Print

November 06, 2015 10:15:05 AM

Page 7

Work Order ID: 138649

138649

Parent Item: D350-748-203

D350-748-203

Parent Item Name: AS350 / AS355 Stainless Steel Aft Crosstube

Start Date: 11/6/2015

Required Date: 11/20/2015

Start Qty: 1.00

Required Qty: 1.00

AN5-32A

Purchased No

220

Each

219.0000

4

4

AN5-32A

Bolt

**

NOV 26 2015

DAS

6

9-89

DAS

28

9-89

DAS

27

9-89

Location

Loc Qty

Loc Code

ST299A

180

m132857

30

m133323

150

ST336

32

m132536

32

ST337

7

m131139

7

D3500-1

Manufactured No

220

Each

11.0000

4

4

D3500-1

Saddle

**

JAN 14 2016

DAS

6

9-89

DAS

28

9-89

Location

Loc Qty

Loc Code

ST406

11

129373

10

131168

1

AN4-6A

Purchased No

220

Each

662.0000

16

16

AN4-6A

BOLT

**

Location

Loc Qty

Loc Code

CA

143

M128403

43

M130851

100

ST325A

100

M133363

100

ST345

419

M128403

8

M133316

411

DAS

6

9-89

DAS

28

9-89

NOV 26 2015

DAS

28

9-89

Item	Qty -243	Part Number	Description
1	X	D350-748-243	CROSSTUBE ASSEMBLY (AS 350/355 HI AFT)
2	1	D8021-125	CROSSTUBE
3	2	D3502-1	SUPPORT
4	2	D5123-7	CLAMP CUSHION
5	1	AETC-1032	INSERT
6	2	MS21920-20 OR MS21920-21/-22	CLAMP (PER DART SPEC. M-MS21920-20/-21/-22)
7	1	NAS1149C0363R	WASHER (OR AN960C10)
8	1	NAS1635-3-8	SCREW (OR MS51958-63)
9	A/R	PROSEAL 890 B-2	SEALANT, AMS-S-8802 CLASS B-2

GENERAL NOTES:

- 1) MATERIAL: MANUFACTURED FROM D8021-125
FINISHED LENGTH AFTER TURNING = 124.70±0.06 (AFTER BENDING/TRIMMING = 122.70 REF)
- 2) FINISH: PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 3) TOLERANCE: PER DART QSI 018 UNLESS OTHERWISE NOTED.
WALL THICKNESS ECCENTRICITY PER DART QSI 038 7.2
MIN. ALLOWABLE WALL IS -0.020 FROM NOMINAL
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED.
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX.
- 6) IDENTIFICATION: DART PART NUMBER "D350-748-243" AND BATCH NUMBER ON INSIDE OF CUFF
PER DART QSI 044 6.4 (VIBRATING STYLUS)
- 7) WEIGHT: 29.85 lbs
- 8) PART IS SYMMETRIC ABOUT CENTERLINE, EXCEPT FOR Ø0.280 HOLE.
- 9) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE. WHEN DRILLING HOLES EXTREME CARE MUST BE TAKEN AND CAREFUL DEBURRING PERFORMED TO ENSURE A CLEAN HOLE WITH NO CRACKING/CHIPPING/GROOVES.

TURNING

- 10) BLEND OUT ALL EDGES FROM MACHINING LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH. NOTE: ALL HOLES ARE DRILLED AFTER BENDING.

BENDING

- 11) BEND PROGRESSIVELY WITH A MINIMUM OF 7 PASSES PER SIDE. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D. ON TOP HALF OF BEND, AND 8% ON BOTTOM HALF OF BEND.
- 12) MAX AMPLITUDE OF RIBBLING ALONG BENT PORTION OF THE TUBE IS 0.030 (ZN A1-3)
- 13) MAX TWIST: WITH XTUBE LAYED FLAT ON SURFACE, THE DIFFERENCE BETWEEN CUFF HEIGHTS FROM THE SURFACE MAY BE NO LARGER THAN 0.38 (ZN C1-3).

ASSEMBLY

- 14) TO INSTALL D3502-1 SUPPORT: ABRASE MATING SURFACE OF SUPPORT AND CROSSTUBE WITH 180-GRIT SANDPAPER AND REMOVE RESIDUE WITH MEK (OR EQUIVALENT). APPLY A 0.02" TO 0.05" THICK LAYER OF PROSEAL 890 CLASS B-2 (OR AMS-S-8802 CLASS B-2) SEALANT TO MATING SURFACE OF SUPPORT.
- 15) TORQUE CLAMPS 60 TO 80 IN-LB. ENSURE AT LEAST 1.5 THREADS SHOWING IN SAFETY AND THAT NUT HAS NOT BOTTOMED-OUT AFTER TORQUING. PRIOR TO PACKAGING, RE-CHECK TORQUE ON CLAMPS AFTER PROSEAL 890 SEALANT HAS CURED FOR 72 HOURS.

RELEASED

2015 MAR 18

4' RCN 15-547

UNDER REVIEW

11/15/20

URF 15-541

120155111006

SH 138649

A	NEW ISSUE	CP	15.01.21
REV.	DESCRIPTION	BY	DATE
DESIGN			
DRAWN			
CHECKED	A.P.		
MFG. APPR.			
APPROVED			
DE APPR.			
DATE	15.01.21		

DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWING NO. D350-748-243	REV. A SHEET 1 OF 4
TITLE CROSSTUBE (AS 350/355 HI AFT)	SCALE NTS

COPYRIGHT © 2015 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

8 7 6 5 4 3 2 1

D

D

C


C

B


B

A

A

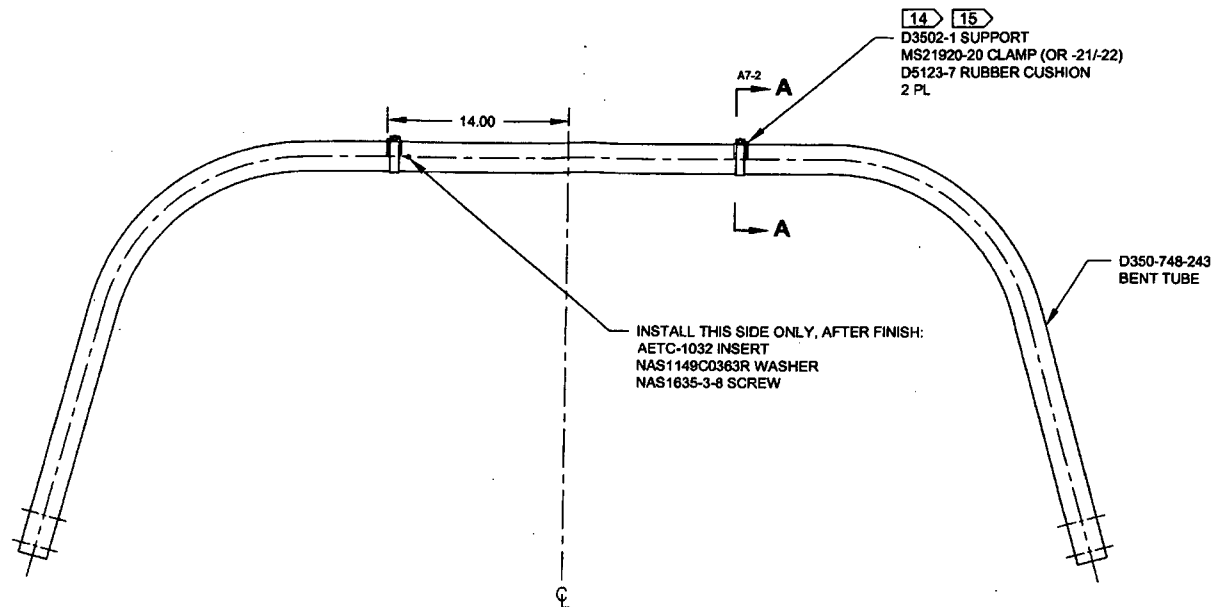

D350-748-243
ASSEMBLY DETAIL

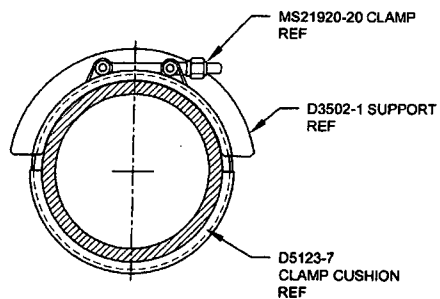

SECTION A-A D4-2
SCALE 6X

UNDER REVIEW

15/4/20

RELEASED

2015 MAR 18

DESIGN	90	DART AEROSPACE LTD	
DRAWN	90	HAWKESBURY, ONTARIO, CANADA	
CHECKED	A.P.	DRAWING NO.	REV. A
MFG. APPR.	<i>[Signature]</i>	D350-748-243	SHEET 2 OF 4
APPROVED	<i>[Signature]</i>	TITLE	SCALE
DE APPR.	<i>[Signature]</i>	CROSSTUBE (AS 350/355 HI AFT)	NTS
DATE	15.01.21	COPYRIGHT © 2015 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR DISSEMINATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

8 7 6 5 4 3 2 1

DQA: _____ Date: _____





WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____


Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐				FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : ☐											

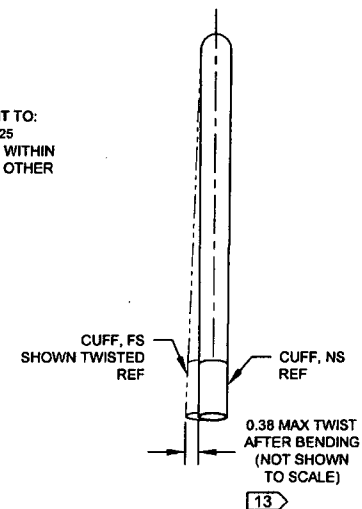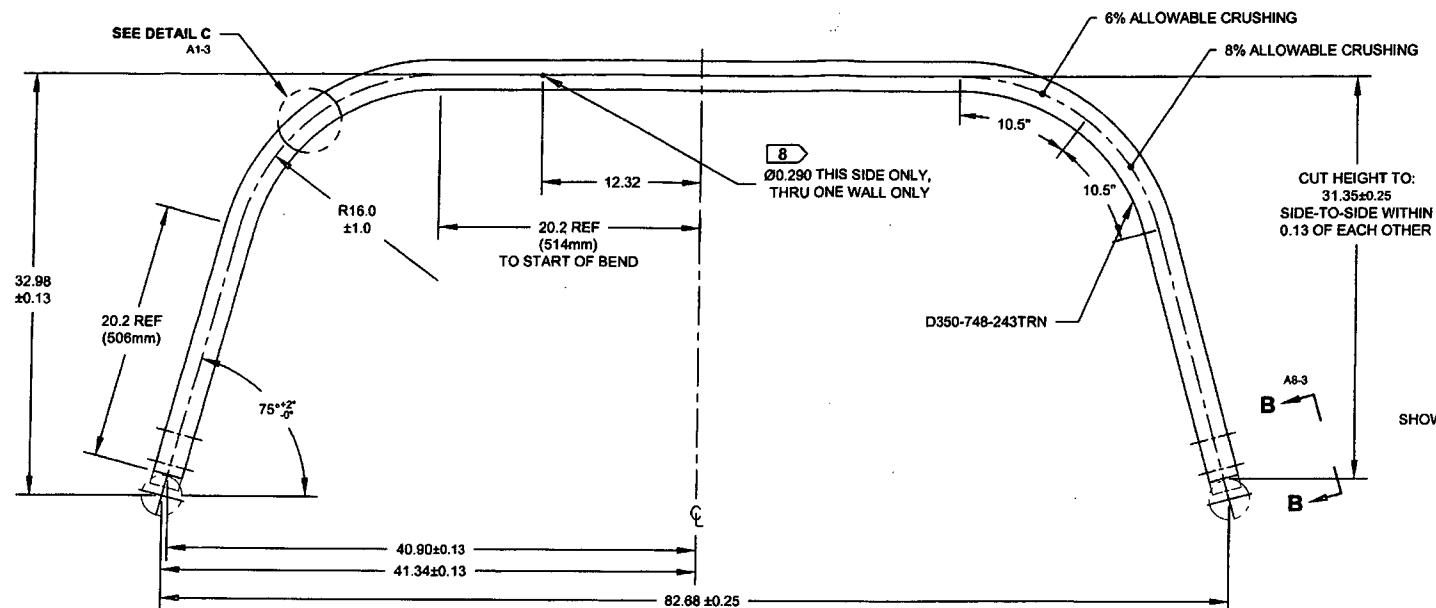

D350-748-243
BENDING AND DRILLING DETAIL 11

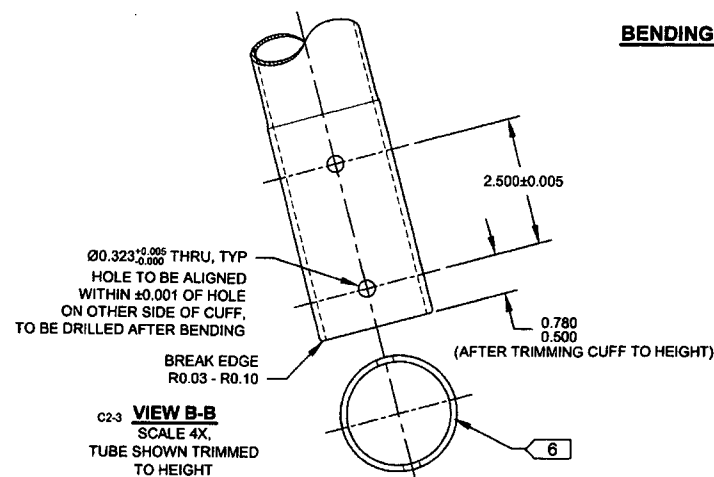


VIEW B-B
SCALE 4X,
TUBE SHOWN TRIMMED
TO HEIGHT

RELEASED

2015 MAR 18

UNDER REVIEW

12 15/4/20

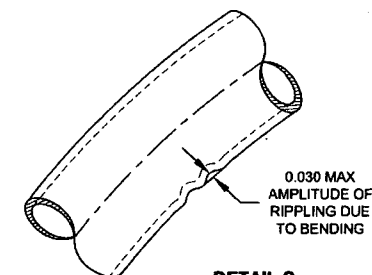

DETAIL C D7-3
SCALE 4X
RIBBLING EXAGGERATED

DESIGN	GP	DART AEROSPACE LTD	
DRAWN	GP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	A.P.	DRAWING NO.	REV. A
MFG. APPR.		D350-748-243	SHEET 3 OF 4
APPROVED		TITLE	SCALE
DE APPR.		CROSSTUBE (AS 350/355 HI AFT)	NTS
DATE	15.01.21	COPYRIGHT © 2016 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR DISCLOSED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐							
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval				
Description Work Order Deviation				Disposition							
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐		No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐		Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐		Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐		Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	
				OTHER : ☐							

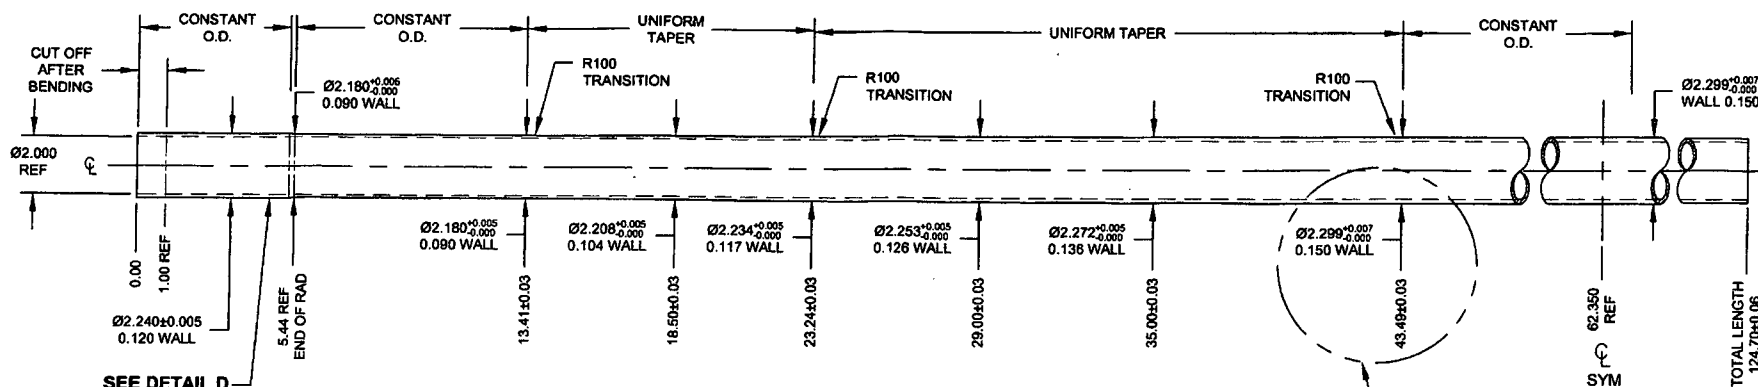


SEE DETAIL D
A6-4

D350-748-243TRN 10
TURNING DETAIL


RELEASE

2015 MAR 18 *q*


SEE DETAIL E
A1-4

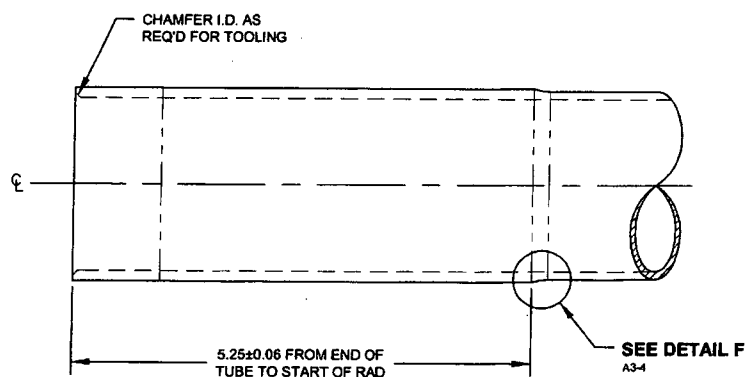

DETAIL D:
CROSSTUBE CUFF C7-4
SCALE 3X

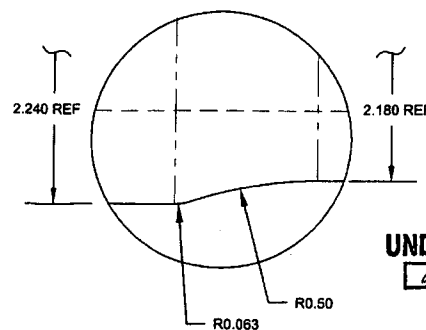

DETAIL F:
CUFF TRANSITION A5-4
NOT TO SCALE

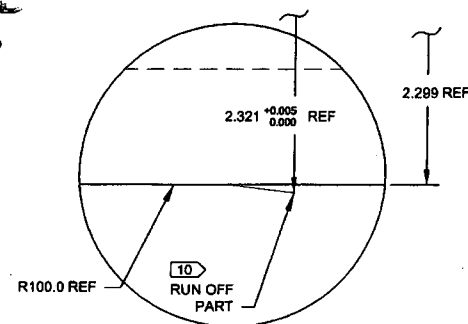

DETAIL E:
TAPER RUN-OFF C2-4
NOT TO SCALE

UNDER REVIEW

15/4/2.9

DESIGN	<i>q</i>	DART AEROSPACE LTD	
DRAWN	<i>q</i>	HAWKESBURY, ONTARIO, CANADA	
CHECKED	<i>AP</i>	DRAWING NO.	REV. A
MFG. APPR.	<i>[Signature]</i>	D350-748-243	SHEET 4 OF 4
APPROVED	<i>[Signature]</i>	TITLE	SCALE
DE APPR.	<i>[Signature]</i>	CROSSTUBE (AS 350/355 HI AFT)	NTS
DATE	15.01.21	COPYRIGHT © 2015 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

DART AEROSPACE LTD		Work Order:	138649
Description: Crosstube High Aft, SS (AS350/355)		Part Number:	D350-748-203
Inspection Dwg: D350-748-243 Rev: A		Page 1 of 1	

Required Dimension	Min	Max
Height	31.10	31.60
1/2 Span	40.77	41.03
Angle	75	77
Total Span	81.54	82.06
Bending Passes	7	--
Crushing	--	8%
Twist	--	0.38

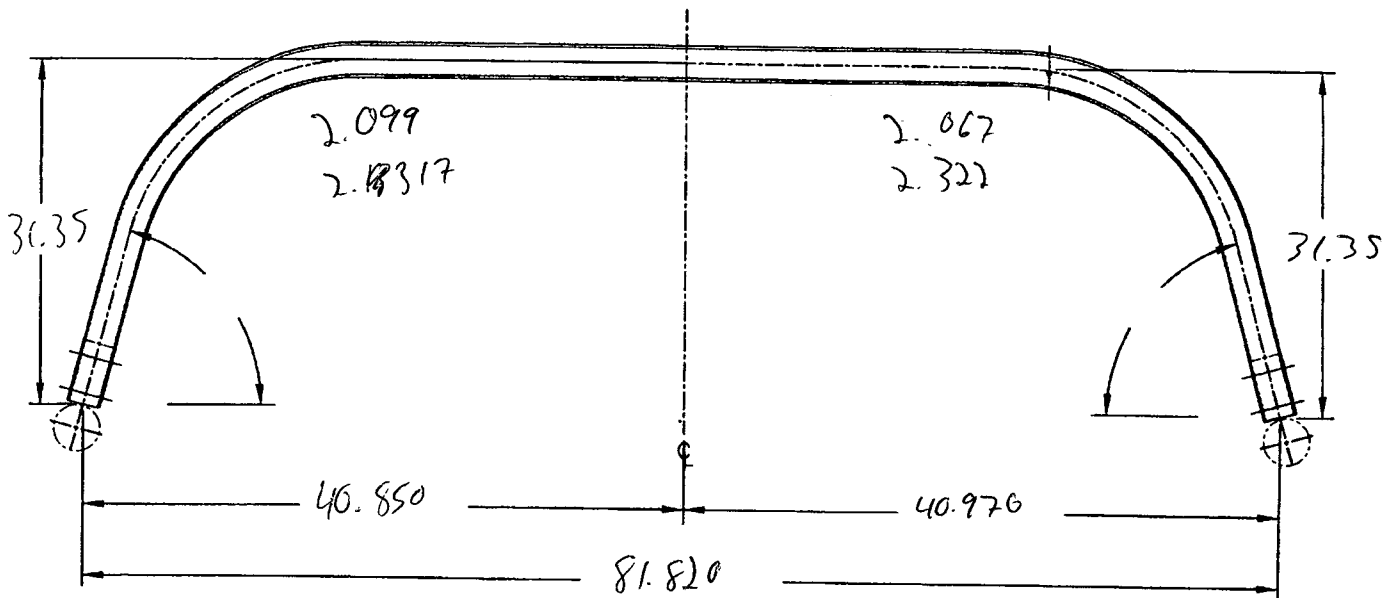

	Side A	Side B
Bending Passes	28	31
Crushing	4.9%	5.8%
Comments		

QC15 Inspection	DAS 03 9:00
Date	15-11-14

Rev	Date	Change	Revised by	Approved
A	15.09.09	New Issue	KJ	



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO30533**

Purchase Order Date 11/20/2015

PO Print Date 11/23/2015

Page Number 4 of 6

Order From :
SKYSERVICE
6120 MIDFIELD ROAD
MISSISSAUGA, ONTARIO L5P 1B1
CANADA

VC-SKY001

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name
Vendor Phone 905-678-5636

Ship To Contact
Ship To Phone
Ship Via: Delivered
Ship Acct:

Buyer
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency CAD
FOB FCA - (Free Carrier)

Line Total: \$115.00

9	138648	D350-748-203 CROSSTUBE	11/23/2015	1.00	\$115.00	\$115.00
---	--------	---------------------------	------------	------	----------	----------

Yes

11/23/2015

SAME AS ABOVE

Line Total: \$115.00

10	138649	D350-748-203 CROSSTUBE	11/23/2015	1.00	\$115.00	\$115.00
----	--------	---------------------------	------------	------	----------	----------

Yes

11/23/2015

SAME AS ABOVE

Line Total: \$115.00

11	138650	D350-748-203 CROSSTUBE	11/23/2015	1.00	\$115.00	\$115.00
----	--------	---------------------------	------------	------	----------	----------

Yes

11/23/2015

SAME AS ABOVE

Note:

11/23/2015

**skyservice****Work Order Traveler**

Sky Service F.B.O. Inc.

DOT APP 53-89 / EASA 145.7142 / BDA AMO,385

WO #: MWO26474	Customer: Dart Aerospace Ltd.	Dept: NDT YUL	Reference: 30533
Descr:	PN:	S/N:	Qty: 1
Make:	Model:	Reg:	A/C S/N:
TSN:	CSN:	TSO:	
Task: UNSCHEDULED			Sequence: 1

Work Required:

CARRY OUT NDT ON 13 CROSSTUBES AS PER PO30533

2 AFT CROSSTUBES, ITEM ID# D212-664-207 , WORK ORDERS ID# 136710, 138508

6 STAINLESS STEEL AFT CROSSTUBES, ITEM ID# D350-748-203 , WORK ORDERS ID# 138647, 138648, 138649, 138650, 138661, 138662

5 STAINLESS STEEL FWD CROSSTUBES, ITEM ID# D350-748-103 , WORK ORDERS ID# 137437, 137438, 138714, 137436, 137439

SP15-11-23

Action Taken:						Date:	Initial/Stamp:
LPI C/O IAW ASTM E-1417M13 NO CRACK FOUND PEN. ZL-56, MPO13600, UV M-20141, CLEANER SKC-S MPO13923 , DEV. MPO11715						NOV 20 2015	
Description	Location	P/N	Qty	Batch	S/N Off	S/N On	

I certified that the maintenance described above has been performed in accordance with the applicable standard of airworthiness.

Signature:	ACA/SCA Stamp 	Date: NOV 20 2015
Name: RAFIK MELIKIAN		

QA Closed:

Date:

WORK ORDER NON-CONFORMANCE / UPDATE

Work Order update only ☐Work Order: 178649Part No. D350-748-203

NCR No.

DISPOSITION

 Rework ☒
 Scrap ☐
 Use-as-is ☐
 Suspected Unapproved ☐

AGAINST DEPARTMENT/PROCESS

Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐
Large Fab ☐	Composite ☐	Supplier ☐	

Date: 15.11.26

Step #:

QTY Effective:

Description Work Order Deviation

AETC-1032 INSERTS BREAKING ON INSTALLATION

Disposition

BASED ON ENG TESTING IT WAS FOUND THAT INSTALLATION IS MORE RELIABLE IF INSTALLATION PRESSURE (AIR HOSE) IS REGULATED TO 50 PSI AND INSTALLATION HOLE IS REAMED TO Ø 0.290 IN ACCORDANCE MANUFACTURERS INSTRUCTIONS. OPEN PART TO ADD NOTE TO STEP # 200 WHICH READS "LIMIT AIR PRESSURE TO 50 PSI WHEN INSTALLING AETC-1032 INSERT AND ONLY EXPAND INSERT ONCE"

MRB (QSI042) Approval

AL

15.11.26

Completed By

Lead hand / Supervisor
Approval VerificationQC / QA Coordinator
Approval

Root Cause

Environment ☐	No Re-verification ☐
Design ☐	Operator ☐
Doc/Data ☐	Offset/Setup ☐
Equip/Tooling ☐	Supplier ☐
Handling/Pre ☐	Training ☐
Material ☐	Use for Testing ☐
Internal Transport ☐	Poor Information ☐
Tribal Knowledge ☐	Rushing ☐
LOA ☐	Product Improvement ☐
Substation ☐	Process Improvement ☐
Past Expiry Date ☐	Manufacturing Process ☐
Misidentified ☐	Past Due ☐

Pressure/Forced

Bending

Centre Not Concentric

Cracks

Crimp/Kink/Ripple/Wave

Cuffs

Crushing

Heat Treat

Wave/Twist in Tube

Marks/Chatter

OTHER:

FAULT CATEGORY

Temperature/Cure

Set-up

BOM/Route

Broken/Damage/Defect

Inspection Incomplete/Unqualified

Contamination

Countersink

Cut Too Short

Instructions Incomplete/Unclear

Drill Holes

Power Loss/Surge

Folio/Program

Grain

Weld

Wrong Stock Pulled

Out of Sequence

Off-set

Misabeled

Fit/Function

Misaligned/off center

Positioned Wrong

Outside Dimensions

Over/Under tolerance

Part Incorrect

Part Lost/Missing

Part Moved

Drawing

Finish

Misread

Turning Sequence

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☒

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☒ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☒ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : <u>16-01-19</u>	Step #: <u>200</u>	QTY Effective : <u>①</u>		MRB (QSI042) Approval DAS 9 9-89 <u>16-01-18</u>	
Description Work Order Deviation		Disposition		Completed By DAS 10 9-89 <u>16-01-19</u>	
AETC-1032 inserts breaking on installation P.C. equipment, no air regulator on tool		had on work order to limit air pressure to 50 psi when installing AETC-1032 insert		Lead hand / Supervisor Approval Verification DAS 9 9-89 <u>16-01-19</u>	
QC / QA Coordinator Approval DAS 9 9-89 <u>16-01-19</u>					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☒ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ ☒ Broken/Damage/Defect Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					
